

Project Portfolio Management (PPM)

Complete Module Reference

Project Financial Mgmt | Planning | Resource Mgmt | Execution | Grants | Integration

PFM

PPL

RES

EXE

GRT

INT

RPT

ORACLE FUSION PPM — COMPLETE MODULE LANDSCAPE

PF
M

Project Financial Management

- + Project Costing
- + Project Billing
- + Project Revenue
- + Budget & Forecast

PP
L

Project Planning & Scheduling

- + Work Breakdown Structure
- + Gantt / Scheduling
- + Baseline Management
- + Milestone Tracking

RE
S

Project Resource Management

- + Resource Demand
- + Resource Supply
- + Team Assignment
- + Utilisation Analytics

EX
E

Project Execution & Control

- + Task Management
- + Issue & Change Mgmt
- + Risk Register
- + Progress Reporting

GR
T

Grants Management

- + Award Management
- + Budget Control
- + Compliance & Audit
- + Effort Reporting

IN
T

PPM Integrations & Config

- + GL/AP/AR/FA Links
- + OIC Integrations
- + FBDI Data Loads
- + Security Model

All PPM modules share a common project data model — seamless flow from planning through financial close without data re-entry.

PROJECT FINANCIAL MANAGEMENT — COSTING, BILLING & REVENUE

Project Costing

Transaction Sources

Labour, Expense, AP, Inventory, Misc

Cost Distribution

Breakdown by task, resource, period

Burdening

Overhead via burden schedule rates

Capitalisation

CIP journal to Fixed Asset transfer

Cost Adjustments

Split, transfer, reverse expenditures

Expenditure Types

Classify and control all cost flows

Project Billing

Billing Events

Milestone or time-based billing triggers

Invoice Generation

Customer invoices generated via AR

Bill Rates & Overrides

Role, resource, or task-level rates

Multi-Currency Billing

Invoice in client's billing currency

Retention

Hold % released on project completion

Credit Memos

Invoice adjustments and write-offs

Project Revenue

Revenue Methods

Cost-to-cost, milestones, units delivered

Revenue Recognition

Automated via accounting events

Unbilled Receivables

WIP balance tracked in GL

Unearned Revenue

Advance billing liability account

Revenue Budget

Plan vs actual revenue tracking

FAH/SLA Integration

Full subledger accounting entries

PFM is the financial backbone of Oracle PPM — every cost flows through costing, then billing, then revenue recognition via FAH/SLA to the General Ledger.

PROJECT PLANNING, SCHEDULING & RESOURCE MANAGEMENT

Project Planning & Scheduling

Work Breakdown Structure (WBS)

Hierarchical task decomposition up to 10 levels. Links to financial structure for cost and billing control.

Project Scheduling

Dependencies (FS/SS/FF/SF), critical path, lag/lead times. Gantt view in Redwood UI from Release 24B+.

Baseline Management

Capture approved scope, schedule, and cost baseline. Compare actuals vs multiple baselines simultaneously.

Budget & Forecast

Budget by task, resource, period. Versions: original, revised, ETC. Integration with EPM for corporate planning.

Milestone Tracking

Key checkpoints tied to billing events or deliverables. Earned value and status calculations per milestone.

Progress & Earned Value

Physical % complete, EV, CPI, SPI, EAC, VAC. Published to stakeholders via OTBI dashboards.

Project Resource Management

Resource Pool & Org Structure

Define centralised or project-managed resource pools by organisation or department hierarchy.

Resource Demand Planning

Forecast requirements by role, skill, and period from WBS task assignments across all projects.

Resource Supply & Availability

Track available capacity from HR org. Identify gaps between demand and supply across the portfolio.

Named Resource Assignment

Assign specific employees or contingent workers to tasks. Replacement and delegation workflows.

Utilisation Analytics

Billable vs non-billable hours, bench time, over/under allocation. Published via OTBI dashboards.

Labour Cost & Rate Schedules

Bill rates, cost rates, and transfer prices by role, employee, or org. Effective-dated rate schedules.

PROJECT EXECUTION, CONTROL & GRANTS MANAGEMENT

Project Execution & Control

Task Management

Assign, track, and complete project tasks. Resource status updates feed back to the project plan automatically.

Issue Management

Log, prioritise, assign, and resolve issues. Linked to tasks and risks with full escalation and audit trail.

Change Orders

Scope change requests with approval workflow. Impact analysis on approved budget, schedule, and revenue contract.

Risk Register

Identify, score (probability x impact), and define mitigation. Linked to contingency reserve budget allocation.

Grants Management

Award & Funding Management

Set up awards, funding sources, sponsors, and terms. Link awards to projects and tasks for cost allocation control.

Grants Budget Control

Hard/soft budget limits per award. Auto-holds on budget overrun. F&A (indirect cost) rate calculations.

Compliance & Audit

Federal OMB Uniform Guidance (2 CFR 200). Cost share, subcontractor tracking, and allowability review.

Effort Reporting

Payroll certification against award-funded effort. PI sign-off workflows. HCM payroll integration for labour.

Oracle Fusion PPM — Project Types

Capital

CIP to FA capitalisation

Contract

Billing & revenue

Indirect

Overhead collection

Time & Material

Cost-plus billing


Fixed Price

Milestone billing

Grants

Award-funded

PPM INTEGRATION ARCHITECTURE — CONNECTIONS TO THE ORACLE ECOSYSTEM

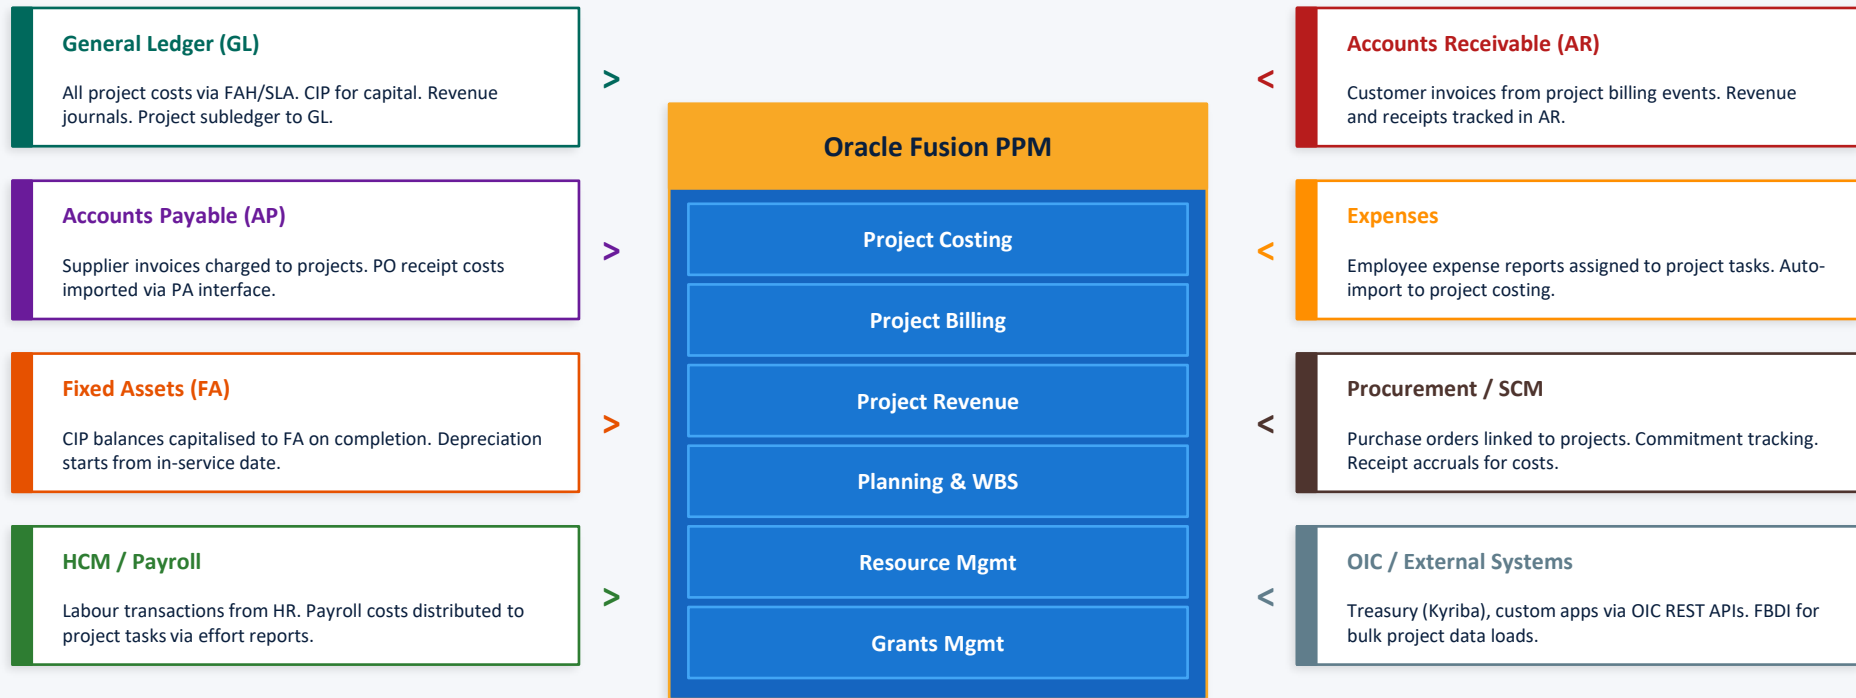

PPM uses the PA Interface and FAH/SLA for all financial transactions — GL is always the financial system of record.

PPM SOLUTION ARCHITECTURE — CONFIGURATION HIERARCHY & REPORTING

PPM Configuration Hierarchy

L1

Project Unit

Top-level PPM business unit. Controls rates, currency, and accounting options.

L2

Project Type

Capital, Contract, Indirect, or Grants template. Drives billing method and accounting.

L3

Project Template

Predefined WBS, team, billing terms, and budget stamped onto new projects at creation.

L4

Project

Individual project record with dates, budget, team, tasks, billing terms, and contract.

L5

Task / Work Package

Chargeable flag controls whether costs can be incurred. Links WBS to financial structure.

L6

Expenditure Type & Item

Cost classification. Maps to Natural Account via Autoaccounting derivation rules.

Autoaccounting Rules

- >> Derive GL account segments from project attributes
- >> Rules by: Project Type, Expenditure Type, Task, Org
- >> Supports Constant, SQL, and PL/SQL derivation types
- >> Separate rules for Cost, Revenue, Billing, and Unearned

PPM Reporting Tools

OTBI — Real-time project cost, billing, resource utilisation subject areas

BI Publisher — Formatted project invoices, budget, and status reports

FAW — Pre-built project KPIs: margin, utilisation, EAC, SPI, CPI

Smart View — Excel-based project budget vs actuals with OTBI connectivity

Project Performance — Redwood performance dashboard (Release 24B+)

SENIOR DELIVERY ARCHITECT — KEY TALKING POINTS FOR YOUR INTERVIEW

End-to-End PPM Ownership

Delivered full PPM lifecycle across Capital (CIP to FA), Contract (T&M and Fixed Price), and Grants — including Autoaccounting, FAH rules, OIC integrations, and OTBI reporting.

Workshop & CRP Leadership

Led solution design workshops, CRP1/CRP2/UAT sessions, and business process walkthroughs with CXO-level Finance and PMO stakeholders across multiple industries.

Multi-Phase Programme Delivery

Managed multi-phase Oracle Cloud programmes with 20-128 resources. Delivered on time using SAFe Agile and waterfall hybrid with full change control and governance.

Complex Integration Architecture

Designed PPM integrations with Kyriba (Treasury), ADP (Payroll), Maximo (Assets), and custom systems via OIC Gen2/Gen3, FBDI, and REST APIs in production.

Billing & Revenue Configuration

Deep expertise in chargeable flags, billing schedules, revenue methods (cost-to-cost, milestone, units of delivery), and multi-currency invoice generation.

Grants & Public Sector

Implemented Grants Management for Ministry of Defense (6 military entities, 128 resources, 48 months) and Ministry of Foreign Affairs (132 consulates, 22 months).
